




# B8 Basement P2

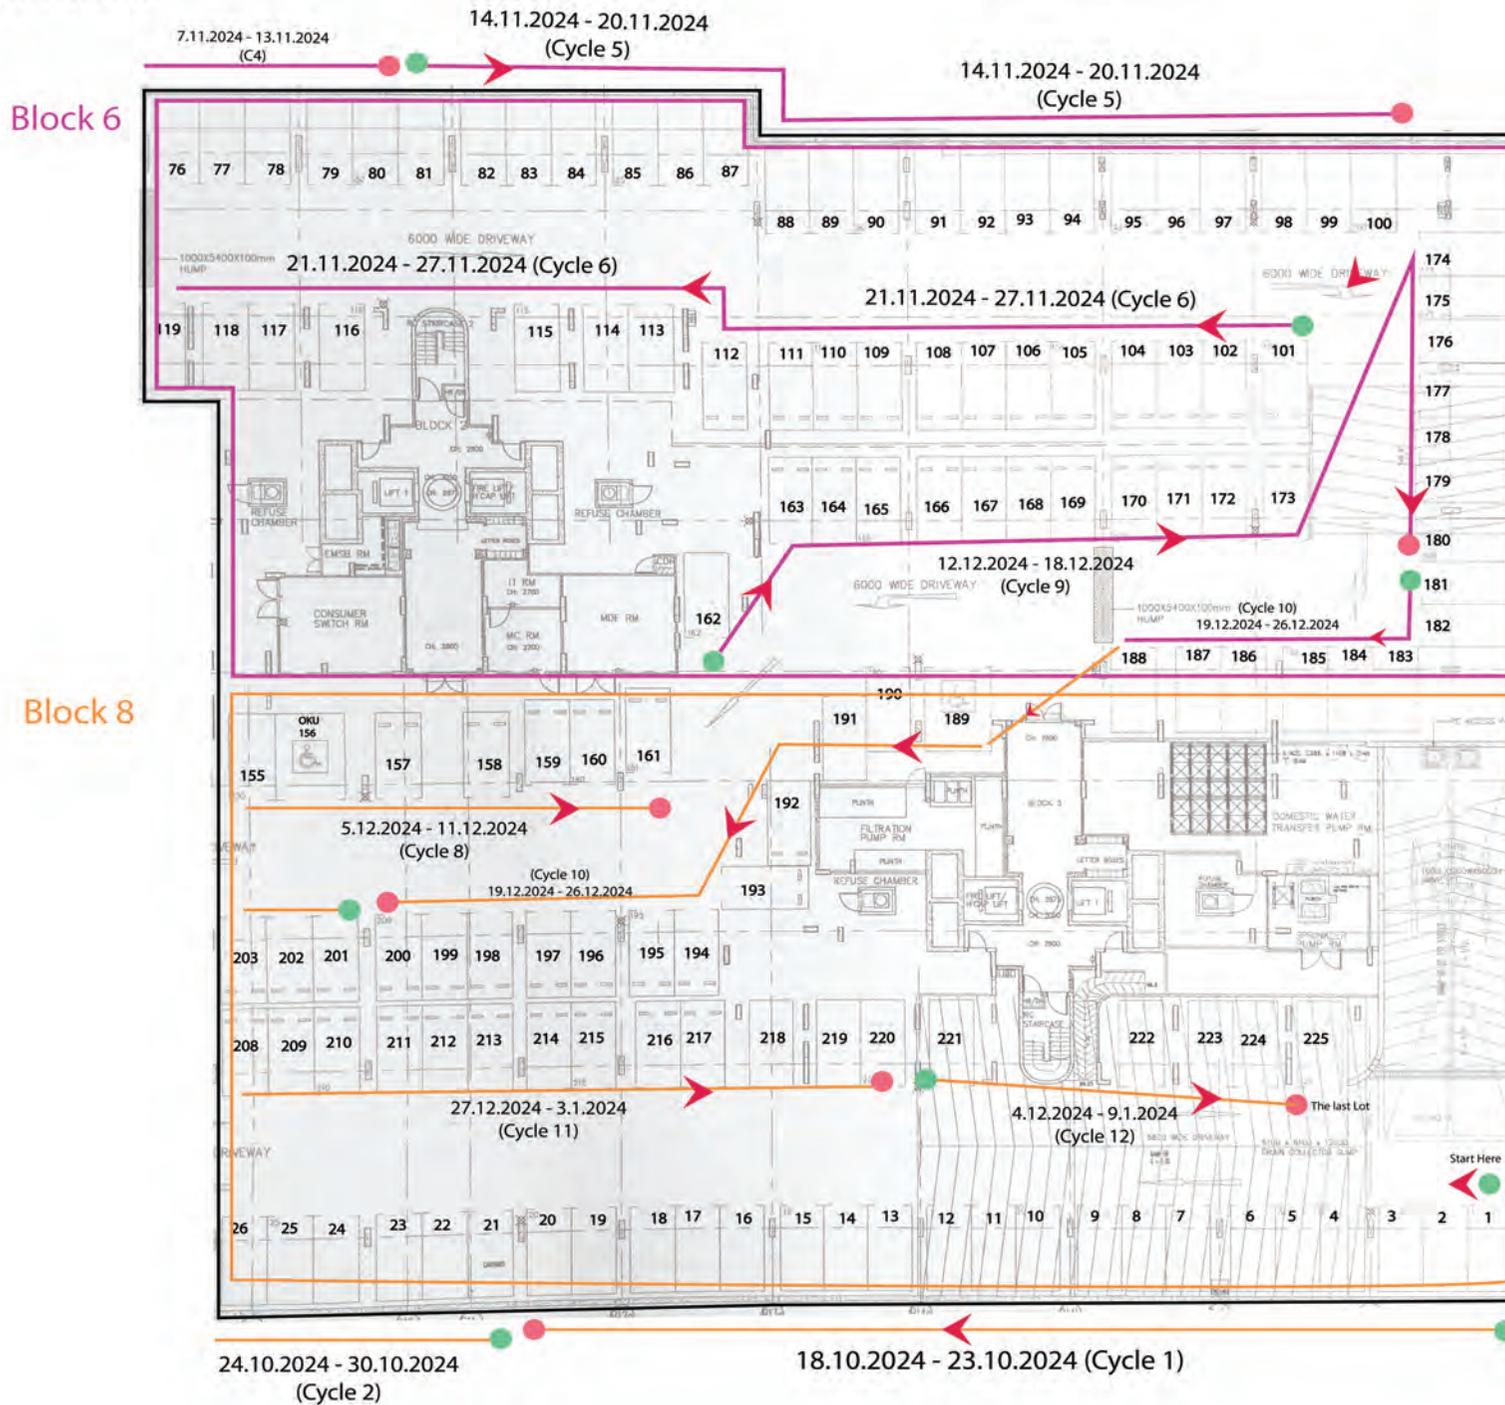

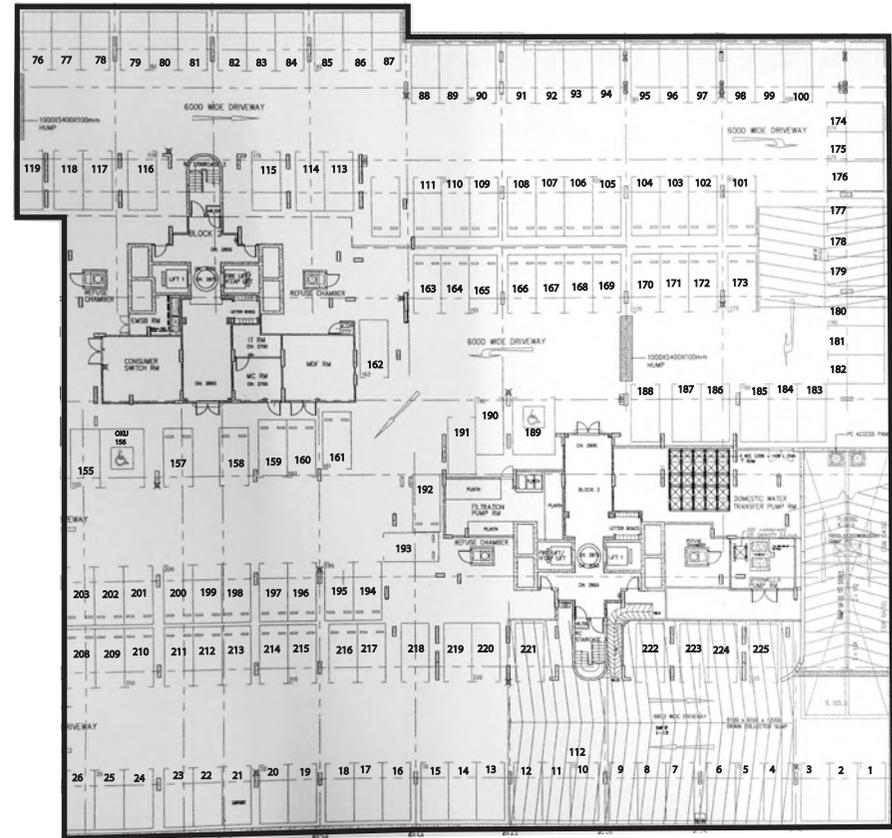

# B8 Basement Full

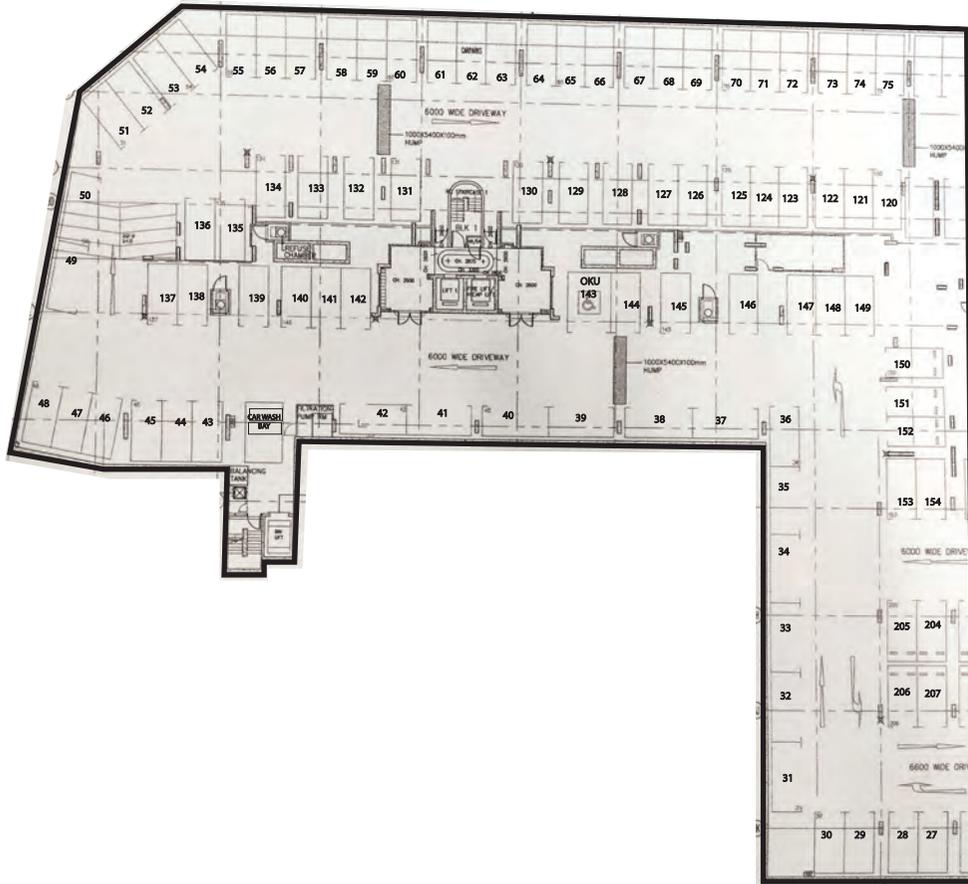

**PROPOSED REPAIRS AND REPAINTING WORKS AT BUTTERWORTH  
8 SINGAPORE**

<b>Cycle 1</b>	<b>Start</b>	<b>Complete</b>
Lots 1 – 20 (Block 8)	18/10/2024	23/10/2024

<b>Cycle 2</b>	<b>Start</b>	<b>Complete</b>
Lots 21 - 26 (Block 8) Lots 27 - 35 (Block 2) Lots 36 - 40 (Block 8)	24/10/2024	30/10/2024

<b>Cycle 3</b>	<b>Start</b>	<b>Complete</b>
Lots 41 – 48 (Block 2) Lots 49 - 54 (Block 2) Lots 55 - 60 (Block 2)	1/11/2024	6/11/2024

<b>Cycle 4</b>	<b>Start</b>	<b>Complete</b>
Lots 61-75 (Block 2) Lots 76-80 (Block 6)	7/11/2024	13/11/2024

<b>Cycle 5</b>	<b>Start</b>	<b>Complete</b>
Lots 81-87 (Block 6) Lots 88-100 (Block 6)	14/11/2024	20/11/2024

<b>Cycle 6</b>	<b>Start</b>	<b>Complete</b>
Lots 101- 105 (Block 6) Lots 106-119 (Block 6) Lots 120 (Block 2)	21/11/2024	27/11/2024

***Note: Please note that the above schedule is subject to changes dependent on site and weather conditions or any unforeseen circumstances.***

**PROPOSED REPAIRS AND REPAINTING WORKS AT BUTTERWORTH  
8 SINGAPORE**

<b>Cycle 7</b>	<b>Start</b>	<b>Complete</b>
Lots 121–130 (Block 2) Lots 131 - 136 (Block 2) Lots 137 - 140 (Block 2)	28/11/2024	4/12/2024

<b>Cycle 8</b>	<b>Start</b>	<b>Complete</b>
Lots 141–149 (Block 2) Lots 150-154 (Block 2) Lots 155-161 (Block 8)	5/12/2024	11/12/2024

<b>Cycle 9</b>	<b>Start</b>	<b>Complete</b>
Lots 162-175 (Block 6) Lots 176-180 (Block 6)	12/12/2024	18/12/2024

<b>Cycle 10</b>	<b>Start</b>	<b>Complete</b>
Lots 181–188 (Block 6) Lots 189-193 (Block 8) Lots 194–200 (Block 8)	19/12/2024	26/12/2024

<b>Cycle 11</b>	<b>Start</b>	<b>Complete</b>
Lots 201–203 (Block 8) Lots 204-207 (Block 2) Lots 208-220 (Block 8)	27/12/2024	3/01/2025

<b>Cycle 12</b>	<b>Start</b>	<b>Complete</b>
Lots 221- 225 (Block 8)	4/01/2025	9/01/2025

(Within 60days)

***Note: Please note that the above schedule is subject to changes dependent on site and weather conditions or any unforeseen circumstances.***
